

Projektname: Rauhebergtunnel

Meßreihenr. : 004

Meßrohrname: BK17

Datum : 22.03.23

Meßschritte: 122

Bezugsmessung : 000

Anmerkung :

Schritt Nr.	Verformung pro Meter [mm/m]	Gesamt Verformung [mm]	Kalibrierter Meßwert [µm]
1	0.0014	0.3510	250
2	-0.0483	0.3497	434
3	-0.0103	0.3980	564
4	-0.0195	0.4083	841
5	0.0124	0.4279	143
6	-0.0007	0.4155	779
7	0.0200	0.4162	-1022
8	-0.0019	0.3961	558
9	0.0235	0.3981	-3707
10	-0.0054	0.3746	-5824
11	-0.0012	0.3800	-6544
12	0.0172	0.3812	-5238
13	0.0066	0.3640	-4117
14	0.0031	0.3574	-1850
15	-0.0037	0.3543	-989
16	-0.0169	0.3580	-204
17	0.0274	0.3749	400
18	-0.0095	0.3475	729
19	0.0152	0.3570	750
20	-0.0028	0.3419	895
21	-0.0052	0.3447	815
22	0.0148	0.3499	659
23	-0.0016	0.3351	697
24	-0.0140	0.3367	725
25	0.0144	0.3507	1018
26	0.0023	0.3363	777
27	0.0038	0.3340	742
28	0.0121	0.3302	1274
29	-0.0129	0.3181	1117
30	0.0065	0.3310	946
31	-0.0013	0.3245	906
32	-0.0127	0.3258	867
33	-0.0048	0.3385	887
34	-0.0046	0.3432	753
35	0.0091	0.3478	871
36	0.0061	0.3387	918
37	-0.0056	0.3327	1191
38	0.0016	0.3383	923
39	-0.0053	0.3366	967

Projektname: Rauhebergtunnel
Meßrohrname: BK17
Meßschritte: 122
Anmerkung :

Meßreihenr. : 004
Datum : 22.03.23
Bezugsmessung : 000

Schritt Nr.	Verformung pro Meter [mm/m]	Gesamt Verformung [mm]	Kalibrierter Meßwert [μ m]
40	-0.0068	0.3420	957
41	-0.0035	0.3488	1095
42	0.0094	0.3523	1049
43	-0.0049	0.3429	1020
44	-0.0048	0.3478	929
45	0.0064	0.3526	1121
46	-0.0110	0.3463	1120
47	0.0102	0.3572	1249
48	-0.0060	0.3470	1071
49	0.0086	0.3530	1332
50	-0.0185	0.3444	1214
51	0.0186	0.3629	1200
52	-0.0043	0.3442	1386
53	0.0065	0.3486	1449
54	-0.0127	0.3421	1399
55	0.0181	0.3548	1225
56	0.0077	0.3367	1229
57	-0.0068	0.3290	1430
58	0.0091	0.3358	1361
59	0.0075	0.3268	1472
60	0.0015	0.3193	1517
61	-0.0064	0.3178	1464
62	0.0011	0.3242	1439
63	-0.0059	0.3231	1464
64	0.0071	0.3290	1781
65	0.0035	0.3219	1483
66	0.0029	0.3184	1546
67	0.0018	0.3155	1658
68	-0.0025	0.3137	1500
69	-0.0013	0.3161	1365
70	0.0029	0.3175	1615
71	0.0053	0.3146	1631
72	-0.0136	0.3093	1709
73	0.0059	0.3229	1586
74	0.0159	0.3170	1880
75	0.0062	0.3011	1726
76	-0.0029	0.2949	1912
77	0.0224	0.2978	1849
78	0.0046	0.2754	1863
79	-0.0039	0.2709	1958

Projektname: Rauhebergtunnel
Meßrohrname: BK17
Meßschritte: 122
Anmerkung :

Meßreihennr. : 004
Datum : 22.03.23
Bezugsmessung : 000

Schritt Nr.	Verformung pro Meter [mm/m]	Gesamt Verformung [mm]	Kalibrierter Meßwert [μ m]
80	-0.0080	0.2748	1632
81	0.0097	0.2829	1658
82	-0.0002	0.2731	1715
83	0.0019	0.2734	1621
84	0.0017	0.2715	1733
85	-0.0014	0.2698	1849
86	-0.0012	0.2711	1721
87	0.0047	0.2723	1743
88	0.0136	0.2676	1774
89	-0.0062	0.2541	2209
90	0.0093	0.2603	1558
91	0.0163	0.2509	1525
92	0.0005	0.2346	1971
93	0.0132	0.2342	2141
94	-0.0029	0.2210	1882
95	0.0208	0.2239	1959
96	-0.0124	0.2031	1498
97	-0.0071	0.2154	1701
98	0.0337	0.2226	1862
99	-0.0211	0.1888	1814
100	-0.0333	0.2099	1661
101	-0.0107	0.2432	1798
102	0.0132	0.2539	1694
103	0.0161	0.2408	1693
104	0.0006	0.2247	1835
105	0.0200	0.2240	1743
106	-0.0041	0.2040	1643
107	-0.0150	0.2081	1631
108	-0.0058	0.2231	1814
109	0.0156	0.2288	1703
110	0.0188	0.2132	1972
111	0.0109	0.1944	1978
112	0.0113	0.1836	2056
113	0.0182	0.1723	2014
114	0.0142	0.1541	1667
115	0.0006	0.1399	1886
116	0.0102	0.1393	1661
117	-0.0192	0.1291	1859
118	0.0532	0.1483	1735
119	0.0212	0.0951	1556

Projektname: Rauhebergtunnel

Meßreihennr. : 004

Meßrohrname: BK17

Datum : 22.03.23

Meßschritte: 122

Bezugsmessung : 000

Anmerkung :

Schritt Nr.	Verformung pro Meter [mm/m]	Gesamt Verformung [mm]	Kalibrierter Meßwert [μ m]
120	0.0208	0.0739	1901
121	0.0635	0.0531	1780
122	-0.0104	-0.0104	1561

Projektname: Rauhebergtunnel

Meßreihennr. : 004

Meßrohrname: BK17

Datum : 22.03.23

Meßschritte: 122

Bezugsmessung : 000

Anmerkung :

Nr	Meßwert abwärts [μm]	Meßwert aufwärts [μm]	mittlerer Meßwert [μm]	Differenz zw. ab u. auf Messung [μm]
1	420	420	420	0
2	605	607	606	-2
3	738	738	738	0
4	1018	1019	1019	-1
5	312	312	312	0
6	956	956	956	0
7	-868	-868	-868	0
8	731	732	732	-1
9	-3587	-3585	-3586	-2
10	-5727	-5730	-5728	3
11	-6465	-6449	-6457	-16
12	-5133	-5138	-5135	5
13	-3999	-4002	-4001	3
14	-1705	-1706	-1706	1
15	-835	-834	-835	-1
16	-41	-39	-40	-2
17	570	573	572	-3
18	912	898	905	14
19	926	926	926	0
20	1074	1072	1073	2
21	992	992	992	0
22	835	833	834	2
23	872	872	872	0
24	902	900	901	2
25	1198	1196	1197	2
26	953	953	953	0
27	917	920	918	-3
28	1457	1456	1457	1
29	1299	1297	1298	2
30	1127	1123	1125	4
31	1085	1083	1084	2
32	1045	1044	1044	1
33	1066	1063	1065	3
34	930	928	929	2
35	1051	1047	1049	4
36	1098	1095	1096	3
37	1375	1371	1373	4
38	1104	1098	1101	6
39	1147	1145	1146	2

Projektname: Rauhebergtunnel
Meßrohrname: BK17
Meßschritte: 122
Anmerkung :

Meßreihennr. : 004
Datum : 22.03.23
Bezugsmessung : 000

40	1138	1133	1136	5
41	1280	1271	1275	9
42	1229	1228	1228	1
43	1202	1196	1199	6
44	1108	1106	1107	2
45	1303	1300	1301	3
46	1305	1297	1301	8
47	1432	1430	1431	2
48	1255	1248	1252	7
49	1518	1513	1515	5
50	1398	1394	1396	4
51	1384	1380	1382	4
52	1572	1567	1569	5
53	1636	1631	1633	5
54	1586	1581	1584	5
55	1408	1405	1406	3
56	1410	1413	1412	-3
57	1615	1614	1614	1
58	1547	1543	1545	4
59	1659	1656	1657	3
60	1705	1700	1702	5
61	1651	1646	1648	5
62	1626	1622	1624	4
63	1651	1647	1649	4
64	1972	1967	1969	5
65	1670	1666	1668	4
66	1733	1730	1731	3
67	1848	1842	1845	6
68	1688	1683	1685	5
69	1551	1546	1549	5
70	1804	1800	1802	4
71	1820	1816	1818	4
72	1900	1894	1897	6
73	1775	1770	1772	5
74	2072	2068	2070	4
75	1916	1912	1914	4
76	2104	2100	2102	4
77	2041	2037	2039	4
78	2055	2050	2053	5
79	2152	2146	2149	6

GLEITMIKROMETER AUSWERTUNG

Anlage 03

Projektname: Rauhebergtunnel
Meßrohrname: BK17
Meßschritte: 122
Anmerkung :

Meßreihenr. : 004
Datum : 22.03.23
Bezugsmessung : 000

80	1822	1816	1819	6
81	1848	1842	1845	6
82	1904	1901	1903	3
83	1812	1803	1808	9
84	1925	1918	1922	7
85	2041	2037	2039	4
86	1912	1907	1909	5
87	1933	1930	1932	3
88	1967	1959	1963	8
89	2404	2403	2404	1
90	1746	1742	1744	4
91	1710	1712	1711	-2
92	2165	2160	2162	5
93	2337	2331	2334	6
94	2073	2072	2072	1
95	2153	2147	2150	6
96	1686	1681	1683	5
97	1891	1886	1888	5
98	2055	2049	2052	6
99	2006	2000	2003	6
100	1850	1847	1849	3
101	1989	1984	1987	5
102	1883	1881	1882	2
103	1883	1879	1881	4
104	2025	2024	2024	1
105	1934	1928	1931	6
106	1832	1829	1831	3
107	1820	1816	1818	4
108	2004	2003	2003	1
109	1892	1890	1891	2
110	2166	2160	2163	6
111	2172	2167	2169	5
112	2251	2246	2249	5
113	2208	2203	2206	5
114	1853	1856	1854	-3
115	2077	2075	2076	2
116	1847	1849	1848	-2
117	2046	2052	2049	-6
118	1921	1925	1923	-4
119	1744	1740	1742	4

GLEITMIKROMETER AUSWERTUNG

Anlage 03

Projektname: Rauhebergtunnel

Meßreihenr. : 004

Meßrohrname: BK17

Datum : 22.03.23


Meßschritte: 122

Bezugsmessung : 000

Anmerkung :

120	2095	2087	2091	8
121	1973	1965	1969	8
122	1750	1744	1747	6

ANLAGE: 03 A

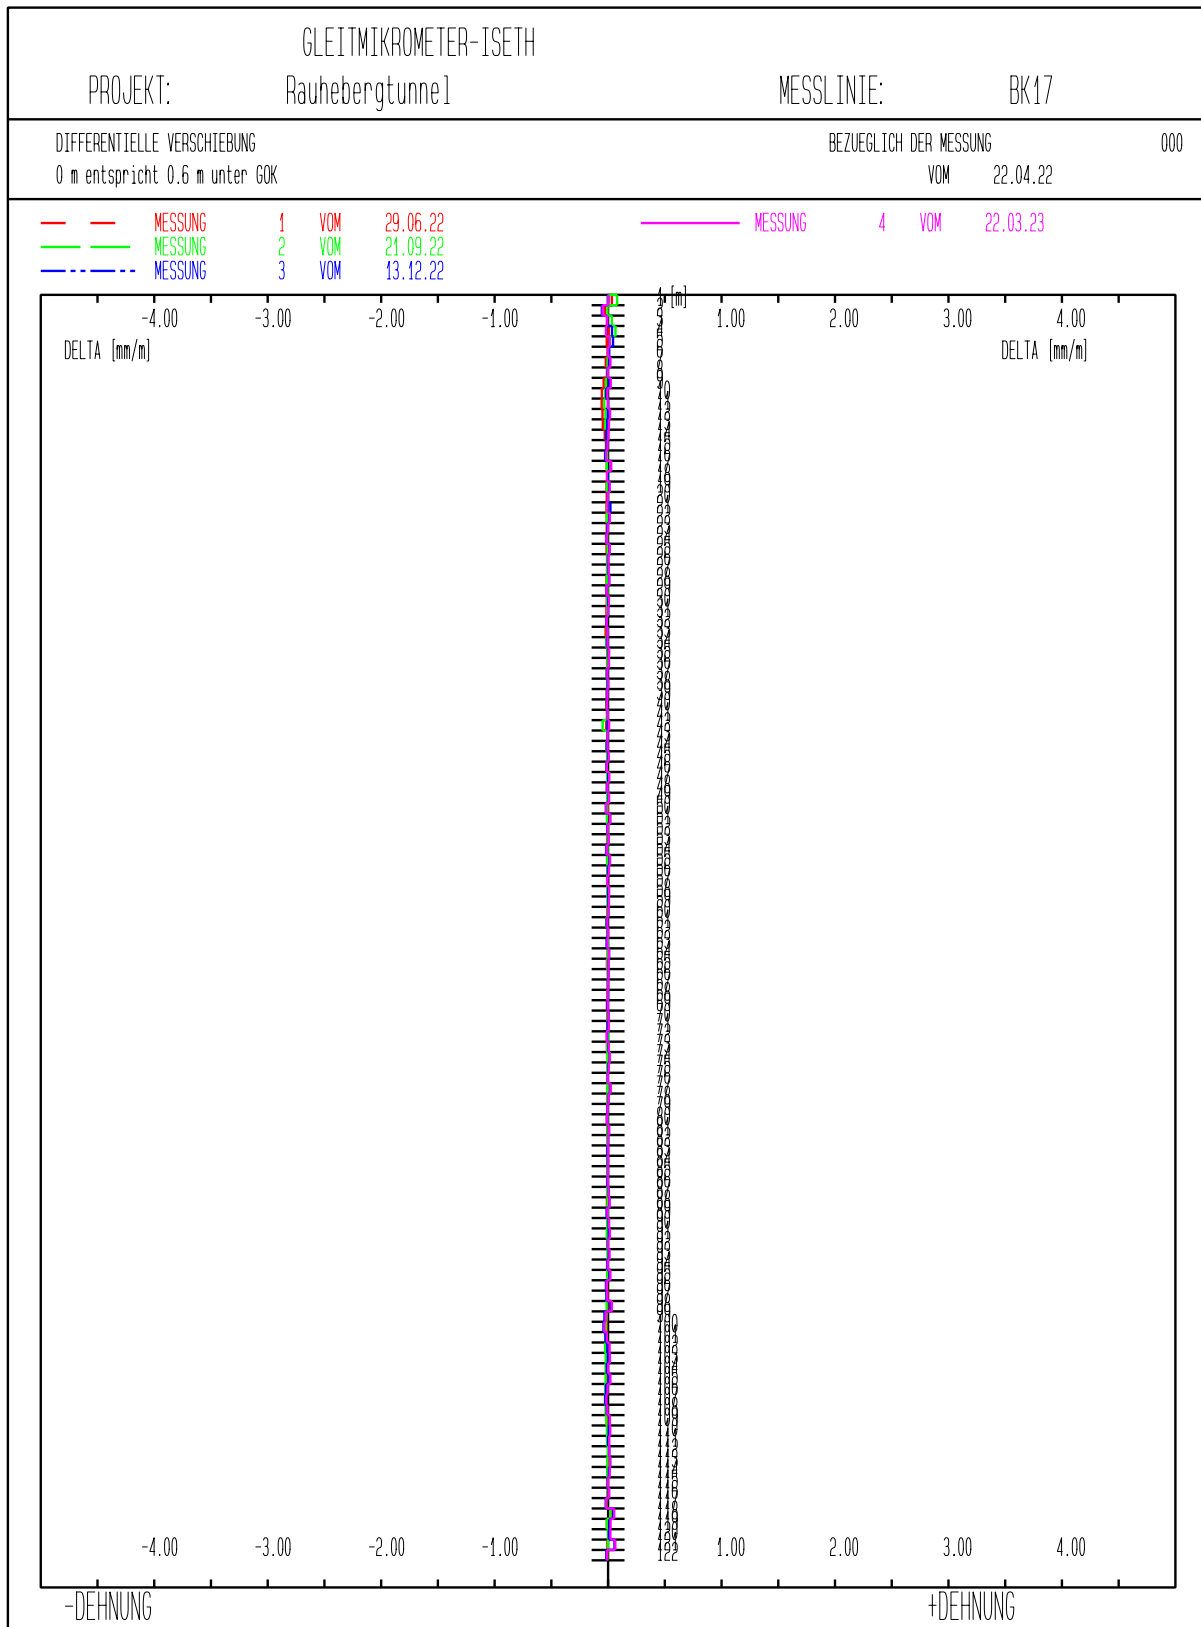

ANLAGE: 03 B

